




**Quality Assurance Management, Inc.**  
1620 Valwood Pkwy, Ste. 128  
Carrollton, TX 75006  
972-331-5800  
QAM.com

# Oxygen Test Report

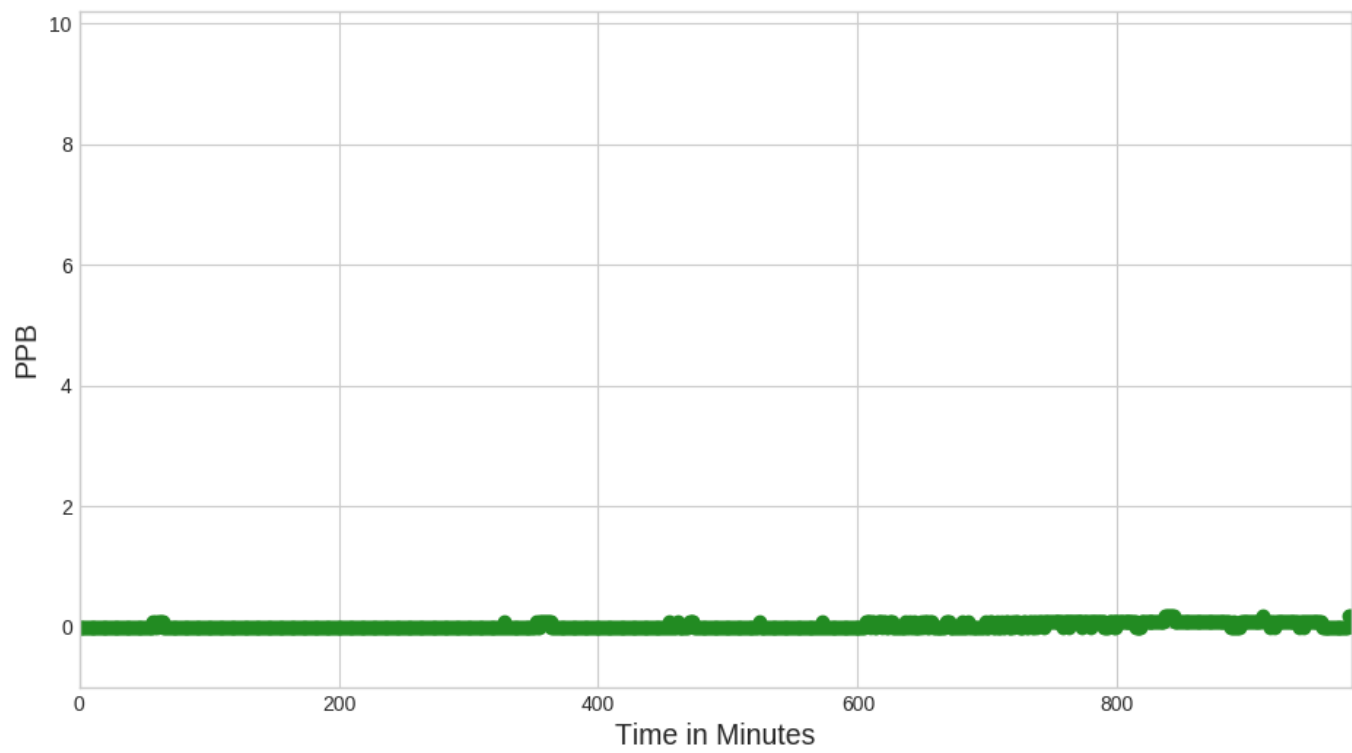


|                      |             |                  |                     |
|----------------------|-------------|------------------|---------------------|
| Client:              | TEST CLIENT | Analyzer:        | Delta F             |
| Facility:            | HQ          | Serial Number:   | PT-18690-V6         |
| Tool / Equipment ID: | TEST123     | Calibration Due: | 7/2021              |
| System:              | PN2         | Instrument Flow: | 2.0 SCFH            |
| Source ID:           | TST-SRC     | Start Time/Date: | 15:13 02/24/21      |
| Test Point ID:       | POC         | Stop Time/Date:  | 07:32 02/25/21      |
| Test Gas:            | Nitrogen    | Test Duration:   | 16 hours 19 minutes |
| Test Flow:           | 4.3 SCFH    | Average:         | 0.0 PPB             |
| Technician:          | JCH         | Final:           | 0.1 PPB             |
|                      |             | Specification:   | 20 PPB              |

Comments:



**Quality Assurance Management, Inc.**  
1620 Valwood Pkwy, Ste. 128  
Carrollton, TX 75006  
972-331-5800  
QAM.com

# Moisture Test Report

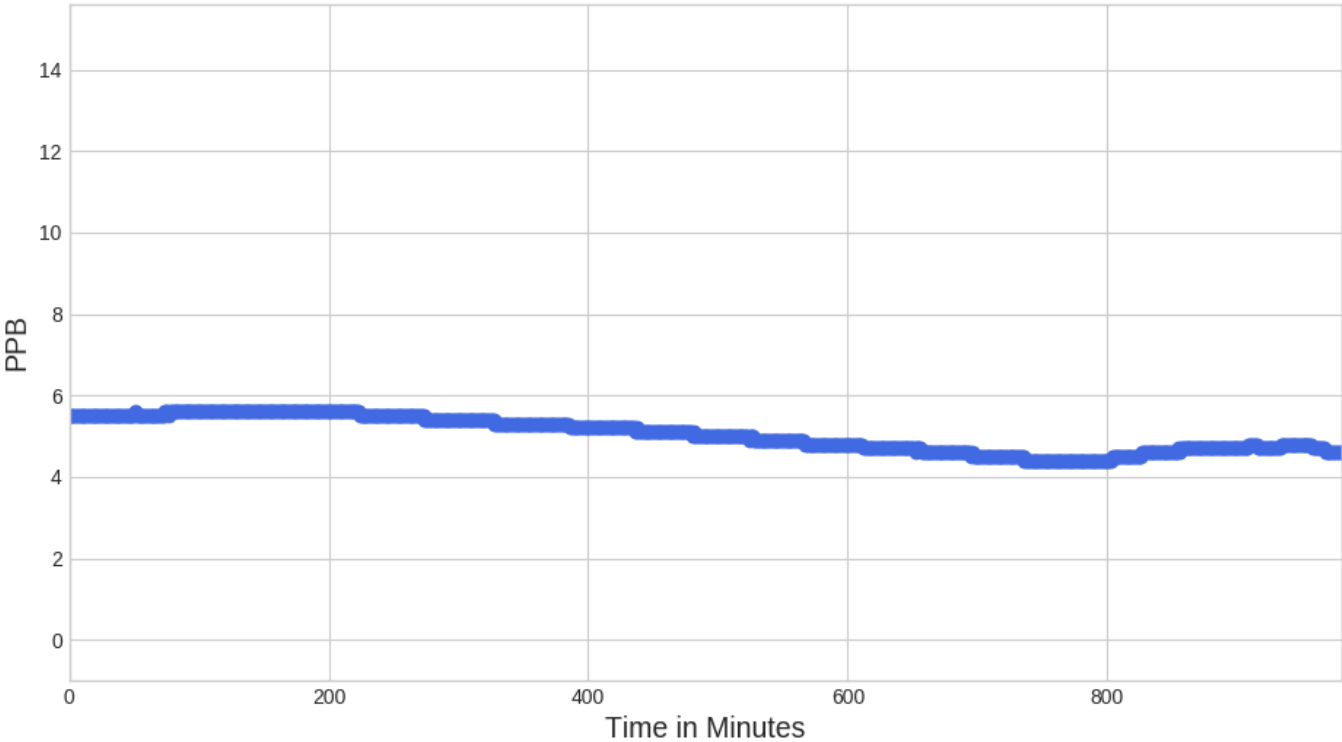

|                      |             |                  |                     |
|----------------------|-------------|------------------|---------------------|
| Client:              | TEST CLIENT | Analyzer:        | Tracer 2            |
| Facility:            | HQ          | Serial Number:   | 17367-44-1          |
| Tool / Equipment ID: | TEST123     | Calibration Due: | 8/2021              |
| System:              | PN2         | Instrument Flow: | 2.3 SCFH            |
| Source ID:           | TST-SRC     | Start Time/Date: | 15:13 02/24/21      |
| Test Point ID:       | POC         | Stop Time/Date:  | 07:32 02/25/21      |
| Test Gas:            | Nitrogen    | Test Duration:   | 16 hours 19 minutes |
| Test Flow:           | 4.3 SCFH    | Average:         | 5.0 PPB             |
| Technician:          | JCH         | Final:           | 4.6 PPB             |
|                      |             | Specification:   | 20 PPB              |

Comments:
