


Comments:

Quality Assurance Management, Inc.

1620 Valwood Pkwy, Ste. 128 Carrollton, TX 75006 972-331-5800 QAM.com

Oxygen Test Report

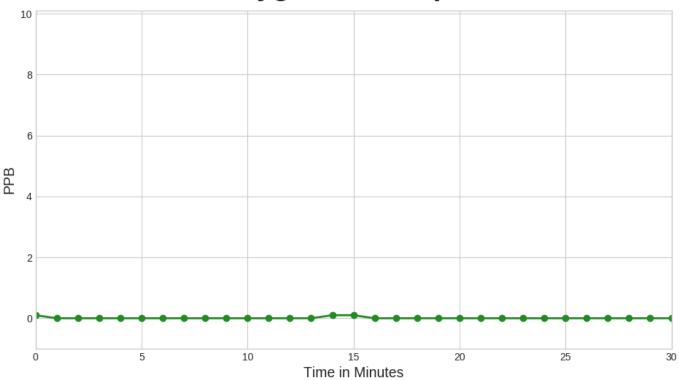


| Client: | TEST CLIENT | | Analyzer: | Delta F | |
|----------------------|-------------|------|---------------------------|----------------|------|
| Facility: | QAM HQ | | Serial Number: | PT-18690-V6 | |
| Tool / Equipment ID: | TEST123 | | Calibration Due: | 7/2021 | |
| System: | PN2 | | Instrument Flow: | 2.0 | SCFH |
| Source ID: | TST-SRC-ID | | Start Time/Date: | 09:53 02/25/21 | |
| Test Point ID: | PN2 POC | | Stop Time/Date: | 10:23 02/25/21 | |
| Test Gas: | Nitrogen | | Test Duration: 30 minutes | | S |
| Test Flow: | 4.3 | SCFH | Average: | 0.0 | PPB |
| Technician: | JCH | | Final: | 0.0 | PPB |
| | | | Specification: | 20 | PPB |



Quality Assurance Management, Inc.

1620 Valwood Pkwy, Ste. 128 Carrollton, TX 75006 972-331-5800 QAM.com

Moisture Test Report

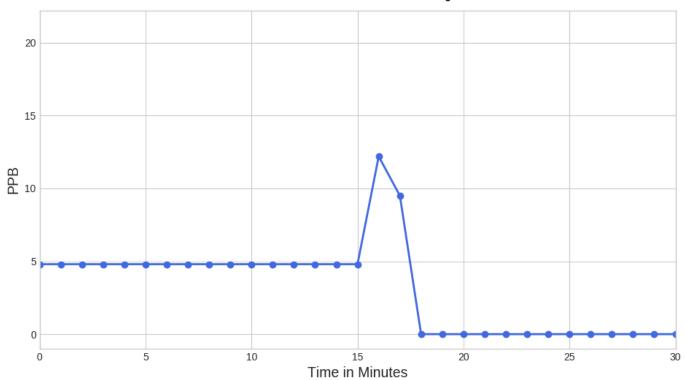

| Client: | TEST CLIENT | | Analyzer: | Tracer 2 | |
|----------------------|-------------|------|------------------|----------------|------|
| Facility: | QAM HQ | | Serial Number: | 17367-44-1 | |
| Tool / Equipment ID: | TEST123 | | Calibration Due: | 8/2021 | |
| System: | PN2 | | Instrument Flow: | 2.3 | SCFH |
| Source ID: | TST-SRC-ID | | Start Time/Date: | 09:53 02/25/21 | |
| Test Point ID: | PN2 POC | | Stop Time/Date: | 10:23 02/25/21 | |
| Test Gas: | Nitrogen | | Test Duration: | 30 minutes | |
| Test Flow: | 4.3 | SCFH | Average: | 3.2 | PPB |
| Technician: | JCH | | Final: | 0.0 | PPB |
| | | | Specification: | 20 | PPB |

| Comments: | |
|-----------|--|
